



KENT WORLDWIDE | KCO2600

2027 Website Design

SOW

SCORO: [HYPERLINK]

FRAMEWORK: [FILL THIS IN]

PROJECT LEAD: [FILL THIS IN]

INT. KO RECORDING: [FILL THIS IN]

June 2026

The Assignment

What are we doing & why:

Kent Worldwide is approaching its 100-year anniversary—a milestone that calls for a website that reflects both the company's refreshed brand and the breadth of its portfolio. Element Three will lead the Design and Functionality phase of this project, producing a web style guide, component designs, functional specifications, and wireframes that serve as the authoritative blueprint for the dev build.

Element Three will also provide extended support through content outlining, build-out consultation, content loading assistance, and pre-launch QA and testing—ensuring the developer has what they need and that the final product meets the vision before the 2027 launch.

What makes that a great experience to hit the target:

KENT hired us because they have said they aren't web experts and need help translating the vision to the development team. Hitting the target means leading the Kent comms team through key decision making and helping them balance long-term website implications with near term vision.

We are their “Easy button.”

Project Description & Scope

What important project details should everyone know?

- #1 - Read the client brief & project proposal
- KENT bid this work out and we won!
- Johnnie (approver) is Leandra's boss, let's make sure to leave a good impression for our friends at GPC and KENT :)

How does this project fit into the larger strategy?

We need to better understand the holistic strategy around the 100 year celebration and how this website will be promoted. The website was not in the annual budget plan but is incredibly important to the Kent family / stakeholders in the company.

DELIVERABLES

- Web style guide
- All component design files
- Functional specification documentation
- Wireframe design files (8 pages)
- Codal hand-off documentation
- Content outlines for new and updated pages
- Copywriting documentation for seven pages

Key Resources

Is there an existing vision or things that must be included?

What is the one unique selling point to be included?

What research and resources are available to inform this work?

Have we done similar work in the past for the client? If so, what was the result?

1. [PROPOSAL](#)
2. [Client Brief](#)
3. [Client Discovery Call](#)

Project Approach

ELEMENT THREE

APPROACH

Element Three will lead Kent Worldwide's website design and content work ahead of its 100-year anniversary launch, producing the full design blueprint and content that Codal needs to build kentww.com. Our work spans a web style guide, component designs, functional specifications, page mockups, content outlines, and copywriting for seven new pages. This is sequenced to keep development moving without waiting on us.

This plan is built to target a mid-November launch, but timing is largely up to Kent and Codal. To expedite our work, we're running design and content in parallel rather than in sequence. The upfront work (discovery, style guide, and module design) gets done early and fast, so specs and page mockups can follow closely behind and Codal has a clear, unambiguous build package in hand by mid-August.

PHASES


- Assessment & Project Design ✓
- Project Kickoff
- Info architecture & Design
- Content development
- Development
- Launch
- Code warranty

TEAM

- Account Executive: Victoria Shaw
- Project Manager: Colton Angel
- Strategist: Brian Cole
- Web & Tech / Project Lead: Rachel Young
- Web & Tech support: Kayla Searles
- Art Direction / Design: Noah Gregg
- Copywriting: Nick Honeywell
- Exec Oversight: John Gough

Milestones & Timeline

ELEMENT THREE

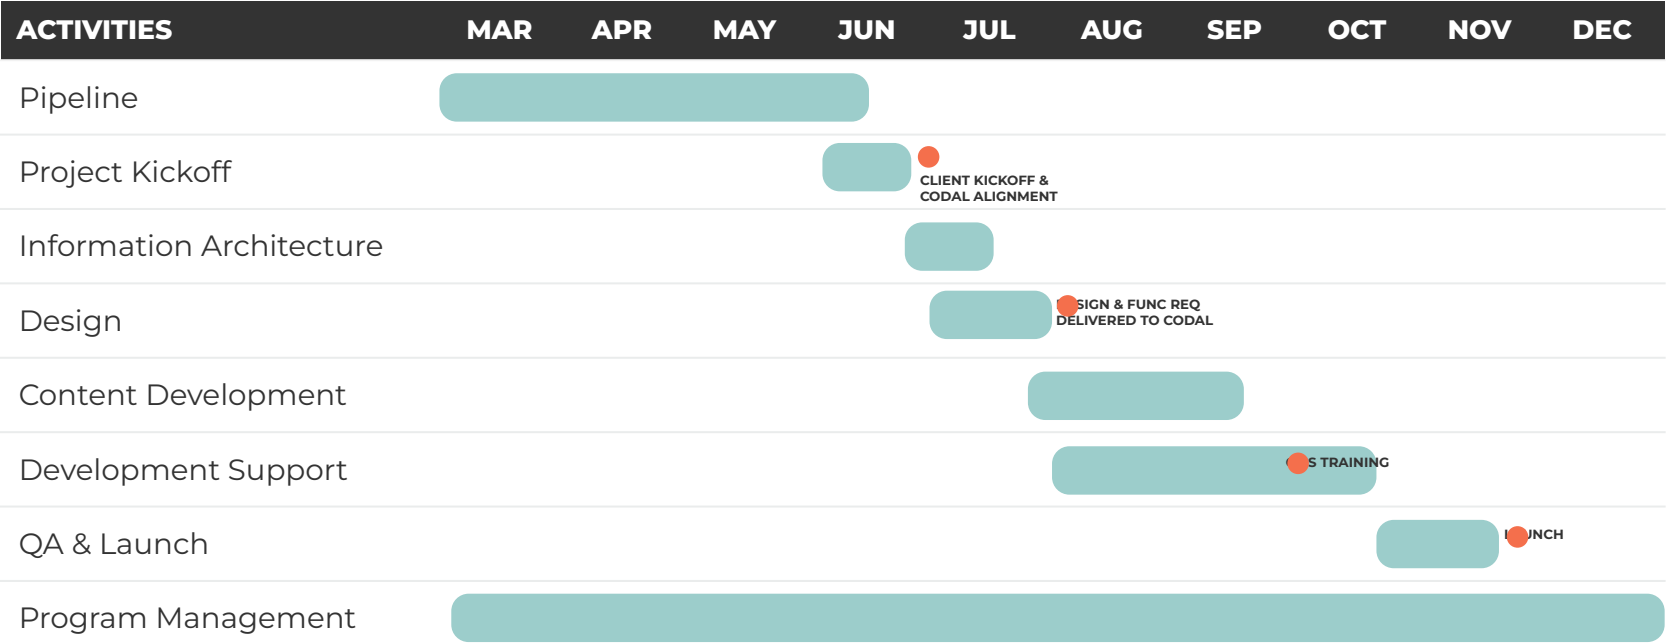

Project Kickoff

ELEMENT THREE

Est. hours: 12 (14% of budget)*

Timeline: June 24 - July 1

TASK / ACTIVITY	DESCRIPTION	START	END	ASSIGNEE	HOURS
Internal Kickoff	Review SOW, brand book, and proposal deck. Align on phases, parallel workstreams, and ownership.	6/24/26	6/24/26	Victoria Shaw, Colton Angel, Rachel Young, Kayla Searles, Noah Gregg, Nick Honeywell, Brian Cole, John Gough	4
Client Kickoff Deck	Build the slides to use in the client kickoff meeting.	6/25/26	6/30/26	Victoria Shaw, Colton Angel	2
Client Kickoff Meeting	Introductions to Leandra and Johnnie. Establish feedback cadence, expectation setting, timeline and where they'll be involved.	7/1/26	7/1/26	Victoria Shaw, Colton Angel, Rachel Young	3
Codal Intros / Kickoff	Review scope, responsibilities, timeline, and delivery methods to ensure alignment of expectations.	7/6/26	7/10/26	Victoria Shaw, Colton Angel, Rachel Young, John Gough	4

*Does not include Pipeline and Delivery (Account Exec, Project Manager, Strategist) general tasks, but they should be accounted for in overall project plan for budget management

Information Architecture

ELEMENT THREE

Est. hours: 28 (9% of budget)

Timeline: June 25 - July 17

TASK / ACTIVITY	DESCRIPTION	START	END	ASSIGNEE	HOURS
Document Existing Modules and Nav Structure	Document existing modules and nav structure. Note accessibility failures for design remediation. Identify backend styling options. Flag constraints for Codal.	6/25/26	6/30/26	Rachel Young/Kayla Searles	8
Draft Content Outlines and Discovery Guide for New Pages	Outlines for all new/updated pages including module selection recommendations. Follow SEO best practices. Recommend module additions to new content on existing pages.	7/1/26	7/7/26	Rachel Young	10
Draft Functionality Write Ups for New Modules & Features	Document behavior, interactions, responsive breakpoints, backend CMS editing, accessibility behaviors (ARIA, keyboard nav) for Codal team.	7/1/26	7/7/26	Rachel Young	2
Discovery Sessions with Kent	Gather content inputs for copywriting, focusing on copy pages. Nick should attend; if not, record.	7/8/26	7/17/26	Rachel Young, Nick Honeywell	8

Design

ELEMENT THREE

Est. hours: 58 (18% of budget)

Timeline: June 25 - July 31

TASK / ACTIVITY	DESCRIPTION	START	END	ASSIGNEE	HOURS
Create Web Style Guide	Translate Kent brand book into web style guide (primary and accent colors, font hierarchy, spacing, buttons, etc.)	6/25/26	6/30/26	Noah Gregg	4
Restyle Existing Modules	All existing modules (14) per the SOW design plan. Desktop and mobile.	7/1/26	7/13/26	Noah Gregg	28
Design New Modules & Features	Homepage carousel, logo carousel, History timeline, News directory and article template. Coordinate with Nick on timeline density. Desktop + mobile.	7/14/26	7/16/26	Rachel Young, Noah Gregg	10
Navigation + Footer Design Options	Main nav: Mars-inspired + 1-2 alts. Footer: as-is style update + lightly reorganized. Desktop + mobile.	7/17/26	7/20/26	Noah Gregg	8
Figma Design Support	Help Noah in Figma as needed.	6/25/26	7/31/26	Rachel Young	8

Design Review

ELEMENT THREE

Est. hours: 10 (3% of budget)

Timeline: July 21 - Aug 3

TASK / ACTIVITY	DESCRIPTION	START	END	ASSIGNEE	HOURS
Style Guide + Component Design - Internal Review	Internal QA + scope completion checklist.	7/21/26	7/22/26	Victoria Shaw, Colton Angel	2
Style Guide + Component Design - Client Review	Schedule and facilitate client QA review.	7/27/26	7/29/26	Victoria Shaw, Colton Angel, Rachel Young, Noah Gregg	4
Dev Handoff Meeting (Design + Functional Specs)	Determine in kickoff if this is one or multiple meetings and how you work together. This is to talk through the changes and new functionality, answer questions, etc.	7/30/26	8/3/26	Victoria Shaw, Colton Angel, Rachel Young, Noah Gregg	4

Prompt for Web Style Guide AI Help

ELEMENT THREE

I need you to build an HTML style guide artifact for a client called KENT WORLDWIDE. I'm attaching two sets of inputs:

1. The KENT WORLDWIDE Brand Book (PDF) — this is your source of truth for all brand decisions including colors, typography, logo rules, and voice.
2. Four screenshots of a web design system from a separate project — these define the format, section structure, and level of detail I need. Do not use any of the visual styles, colors, or fonts from those screenshots. They are structural references only.

Build the style guide as a single HTML artifact with the following four sections, in this order:

Section 1 — Color Palette

Extract all colors from the brand book. Separate primary and secondary palettes. Display each color as a circle with the hex value and color name beneath it, matching the layout format in the color screenshot.

Section 2 — Desktop Typography

Use the desktop type scale from the brand book. The fonts are Roboto (headlines, subheads, callouts), Roboto Serif (body copy), and Meow Script (accent only). Load all three from Google Fonts. Display each type style as a live rendered specimen with the style name, font name, weight, size, and line height labeled, matching the layout format in the desktop typography screenshot.

Section 3 — Mobile Typography

Same as Section 2 but using mobile scale values. Where the brand book does not specify explicit mobile sizes, apply reasonable responsive reductions and note that these are inferred.

Section 4 — Buttons and Interactive States

The brand book does not document button states. Infer a logical and brand-appropriate V1 button system using the primary color palette. Include primary and secondary button variants, each with default, hover/focus, active, focus state, and disabled states, for both light and dark backgrounds. Match the layout format in the button screenshot. Label all states clearly.

Additional requirements:

- This is a disposable working reference, not a client-facing deliverable. Do not brand the wrapper to match Kent.
- Keep the layout clean, well-spaced, and easy to scan.
- Section headers should be clearly labeled.
- Do not include any content from the screenshot design system other than layout structure.

This will still require Art Direction of:

- Mobile type sizes
- Buttons
- General review and oversight

Content Development

ELEMENT THREE

Est. hours: 69 (22% of budget)

Timeline: July 20 - September 2

TASK / ACTIVITY	DESCRIPTION	START	END	ASSIGNEE	HOURS
Copywriting	Innovation, Our Brands, 100 Year Timeline, Pet Care, Food & Hydration, GPC, KENT Nutrition. Prioritize Innovation and Timeline. Draft new modules for existing pages. Dependent upon successful discovery sessions and receipt of Kent-provided resources.	7/20/26	7/31/26	Nick Honeywell	20
Copy - Internal Review	Check brand voice alignment and structural fit with mockups.	8/3/26	8/5/26	Victoria Shaw, Colton Angel, Rachel Young	12
Page Mockups	Add V1 copy to modular page mockups for client review.	8/6/26	8/7/26	Rachel Young	4
Copy - Client Review	Schedule meeting to walk through V1 drafts with Kent and do tutorial on commenting tool (i.e., Ziflow).	8/10/26	8/28/26	Victoria Shaw, Colton Angel	6
Copy - Revisions	Revise copy based on internal and client feedback.	8/6/26	9/2/26	Nick Honeywell	15

Development Support

ELEMENT THREE

Est. hours: 38 (12% of budget)

Timeline: Beginning 8/3; TBD – Contingent on development timeline

TASK / ACTIVITY	DESCRIPTION	EST START	EST END	ASSIGNEE	HOURS
Build-Out Consultation	Review key milestones, clarify design, available for working sessions with Codal if needed. *Change order if the scope increases	8/3/26	10/2/26	Rachel Young, Noah Gregg	10
CMS Training	Codal to walk us through the main CMS sections to prep for content loading.	10/5/26	10/9/26	Rachel Young, Noah Gregg	2
Image Resizing	Prep for content loading by resizing raw images provided by Kent.	8/24/26	8/28/26	Noah Gregg	4
Content Loading	Load the final approved content and imagery in replatformed site CMS in coordination with Kent and Codal.	10/12/26	10/16/26	Rachel Young, Noah Gregg	10
QA & Testing - Pre-Launch	Review built site for design accuracy vs. approved specs and mockups. Flag errors and accessibility gaps to Codal.	TBD	TBD	Rachel Young, Noah Gregg	12

QA & Launch

ELEMENT THREE

Est. hours: 15 (5% of budget)

Timeline: TBD - Contingent on development timeline

TASK / ACTIVITY	DESCRIPTION	START	END	ASSIGNEE	HOURS
Pre-Launch Sign Off with Kent	Final site review with client. Confirm all deliverables are complete, and site is ready/approved for launch.	TBD	TBD	Victoria Shaw, Colton Angel	3
Launch Day Coordination	Coordinate with Kent and Codal on go-live.	TBD	TBD	Victoria Shaw, Colton Angel	2
Post-Launch Check	Confirm site is live. Capture immediate issues for Codal.	TBD	TBD	Rachel Young, Noah Gregg	2
Project Close	Close project in Scoro. Confirm all invoices sent and paid. Conduct project retro.	TBD	TBD	Victoria Shaw, Colton Angel, Rachel Young, Noah Gregg, Nick Honeywell, Brian Cole, John Gough	8

Budget Flighting Estimate

ELEMENT THREE

The back half of this timeline will be lighter than the upfront, and the exact timing is dependent on the development timeline. Assuming no major delays on design or copy approvals, expect about a month of revenue dip before content loading, QA, and launch prep begin.

PROJECT	ESTIMATE
June (includes Pipeline Recognition)	\$8,000
July	\$25,000
August	\$15,000
September	\$4,000
October	\$6,000
November	\$6,000
December	TBD
TOTAL ESTIMATE	\$64,000

Project Risks

ELEMENT THREE

- **Content Delays from Kent**

Discovery sessions front-loaded. We need to flag missing inputs immediately. Content delays may shift copy timeline, image resizing, content loading, and launch date.

- **Stakeholder Disagreement / Unconsolidated Feedback**

- SOW includes 2 revision rounds per deliverable. Kent primary contact consolidates feedback before delivery to E3. Additional rounds = change order.

- **Codal Estimate & Timeline Not Finalized**

- Ask for timeline by June 27, ahead of the intro/kickoff meeting. If Codal's timeline compresses our mid-November expected launch, Colton will need to rearrange the timeline and resourcing.

- **Scope Creep in Build-Out Consultation (10 Hour Cap)**

- Track time daily in Scoro. When you hit 7 hours, notify Victoria and Colton. Codal requests exceeding 10 hours require a change order before hours are committed. *Do this proactively.*

- **Technical Limitations Discovered During QA**

- Document and route to Codal with prioritization. E3 does not own code remediation. Flag to Kent if issues affect launch timing.
